



ID	Nome da Tarefa	Duração	Início	Conclusão	Predt	11 Feb '08							18 Feb '08			
						S	T	Q	Q	S	S	D	S	T	Q	Q
1	<b>Projecto</b>	<b>107 dias?</b>	<b>13-02-08</b>	<b>09-07-08</b>												
2	Repositório	11 dias?	13-02-08	27-02-08												
3	Templates	3 dias?	25-02-08	27-02-08												
4	<b>(F1) Software Concept</b>	<b>94 dias?</b>	<b>13-02-08</b>	<b>20-06-08</b>												
5	<b>(D) Concept Paper</b>	<b>18 dias?</b>	<b>13-02-08</b>	<b>07-03-08</b>												
6	Realização	16 dias?	13-02-08	05-03-08												
7	Revisao 3 (autores, revisores)	2 dias?	06-03-08	07-03-08	6											
8	(D) Change Control Plan	1 dia?	13-02-08	13-02-08												
9	<b>(D) TOP 10 Risk List</b>	<b>18 dias?</b>	<b>13-02-08</b>	<b>07-03-08</b>												
10	Realização	16 dias?	13-02-08	05-03-08												
11	Revisão 3 (autores, revisores)	2 dias?	06-03-08	07-03-08	10											
12	(D)Software Project Log	94 dias?	13-02-08	20-06-08												
13	<b>(F2) Requirements development</b>	<b>35 dias?</b>	<b>25-02-08</b>	<b>11-04-08</b>												
14	(D) Quality Assurance Plan (includes template of code reviews)	5 dias?	25-02-08	29-02-08												
15	<b>(D) Software Development Plan</b>	<b>16 dias?</b>	<b>25-02-08</b>	<b>17-03-08</b>												
16	Realização	14 dias?	25-02-08	13-03-08												
17	Revisão 3 (autores, revisores)	2 dias?	14-03-08	17-03-08	16											
18	<b>(D) User Interface Prototype</b>	<b>26 dias?</b>	<b>25-02-08</b>	<b>31-03-08</b>												
19	Software Requirements Specification	24 dias?	25-02-08	27-03-08												
20	Revisão 3 do restante (autores, revisores)	1 dia?	28-03-08	28-03-08	19											
21	Realização do Protótipo	17 dias?	05-03-08	27-03-08												
22	Insp. Das partes mais complexas	1 dia?	28-03-08	28-03-08	21											
23	Revisão 3 do restante (autores, revisores)	1 dia?	31-03-08	31-03-08	22											
24	<b>(D) System Architecture</b>	<b>11 dias?</b>	<b>27-03-08</b>	<b>10-04-08</b>												
25	Realização	8 dias?	27-03-08	07-04-08												
26	Insp. Das partes mais complexas	2 dias?	07-04-08	08-04-08												
27	Revisão 3 do restante (autores, revisores)	2 dias?	09-04-08	10-04-08	26											
28	<b>(D) Software Test Cases</b>	<b>9 dias?</b>	<b>27-03-08</b>	<b>08-04-08</b>												
29	Realização	8 dias?	27-03-08	07-04-08												

Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08

Tarefa



Tarefa Agregada



Tarefas Externas



Progresso



Marco Agregado



Resumo de Projecto



Marco



Progresso Agregado



Agrupar por Sumário



Sumário

















Dividir




Prazo




ID		Nome da Tarefa	Duração	Início	Conclusão	Prede	11 Feb '08							18 Feb '08			
							S	T	Q	Q	S	S	D	S	T	Q	Q
30		Insp. Das partes mais complexas	1 dia?	07-04-08	07-04-08												
31		revisão 3 do restante (autores, revisores)	1 dia?	08-04-08	08-04-08	30											
32		<b>(D) Additional Spec Doc</b>	<b>7 dias?</b>	<b>03-04-08</b>	<b>11-04-08</b>												
33		Realização	6 dias?	03-04-08	10-04-08												
34		Insp. Das partes mais complexas	1 dia?	11-04-08	11-04-08	33											
35		<b>(F3) Architectural Design</b>	<b>15 dias?</b>	<b>07-04-08</b>	<b>25-04-08</b>												
36		<b>(D) Software Architecture Doc</b>	<b>11 dias?</b>	<b>07-04-08</b>	<b>21-04-08</b>												
37		Realização	10 dias?	07-04-08	18-04-08												
38		Inspeção	1 dia?	21-04-08	21-04-08	37											
39		<b>(D) Software Integration Procedure</b>	<b>10 dias?</b>	<b>09-04-08</b>	<b>22-04-08</b>												
40		Realização	8 dias?	09-04-08	18-04-08												
41		Revisão 3 (autores, revisores)	2 dias?	21-04-08	22-04-08	40											
42		<b>(D) Software Development Plan revised to include a Staged Delivery Plan</b>	<b>5 dias?</b>	<b>21-04-08</b>	<b>25-04-08</b>												
43		Realização	3 dias?	21-04-08	23-04-08												
44		Revisão 3 (autores, revisores)	2 dias?	24-04-08	25-04-08	43											
45		<b>(F4) Detailed Design Stage 1, 2,...,n</b>	<b>14 dias?</b>	<b>11-04-08</b>	<b>30-04-08</b>												
46		<b>(D) Design Doc for this Stage</b>	<b>12 dias?</b>	<b>11-04-08</b>	<b>28-04-08</b>												
47		Realização	11 dias?	11-04-08	25-04-08												
48		Insp	1 dia?	28-04-08	28-04-08												
49		<b>(D) Software Construction Plan for this Stage</b>	<b>13 dias?</b>	<b>14-04-08</b>	<b>30-04-08</b>												
50		Realização	11 dias?	14-04-08	28-04-08												
51		Revisão 3 (autores, revisores)	2 dias?	29-04-08	30-04-08	50											
52		<b>(F5) Coding and debugging for Stage 1, 2,...,n</b>	<b>30 dias?</b>	<b>23-04-08</b>	<b>03-06-08</b>												
53		<b>(Code) Code for this Stage developed</b>	<b>30 dias?</b>	<b>23-04-08</b>	<b>03-06-08</b>												
54		Realização	28 dias?	23-04-08	30-05-08												
55		Insp de 2 módulos	3 dias?	26-05-08	28-05-08												
56		Revisão 3 do restante (autores, revisores)	2 dias?	02-06-08	03-06-08												
57		(D) Outcome of tests in this Stage (Update of Software Test Cases Doc)	18 dias?	07-05-08	30-05-08												
58		<b>(F6) Software Release</b>	<b>96 dias?</b>	<b>28-02-08</b>	<b>09-07-08</b>												

Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08

Tarefa



Tarefa Agregada



Tarefas Externas



Progresso



Marco Agregado



Resumo de Projecto



Marco



Progresso Agregado



Agrupar por Sumário



Sumário










Dividir



Prazo



ID		Nome da Tarefa	Duração	Início	Conclusão	Prede	11 Feb '08							18 Feb '08			
							S	T	Q	Q	S	S	D	S	T	Q	Q
59		(D) Delivery description	11 dias?	26-05-08	09-06-08												
60		Realização	10 dias?	26-05-08	06-06-08												
61		Revisão 3 (autores, revisores)	1 dia?	09-06-08	09-06-08												
62		(Code) Final program completed	41 dias?	04-04-08	30-05-08												
63		Archival Media for everything, docs and code	96 dias?	28-02-08	09-07-08												
64		(D) Project History	12 dias?	02-06-08	16-06-08												
65		Realização	9 dias?	02-06-08	12-06-08												
66		Revisão 2(autores, revisores)	3 dias?	13-06-08	16-06-08												


Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08


Tarefa


Progresso


Marco

Sumário











Tarefa Agregada


Marco Agregado


Progresso Agregado

Dividir











Tarefas Externas


Resumo de Projecto


Agrupar por Sumário


Prazo









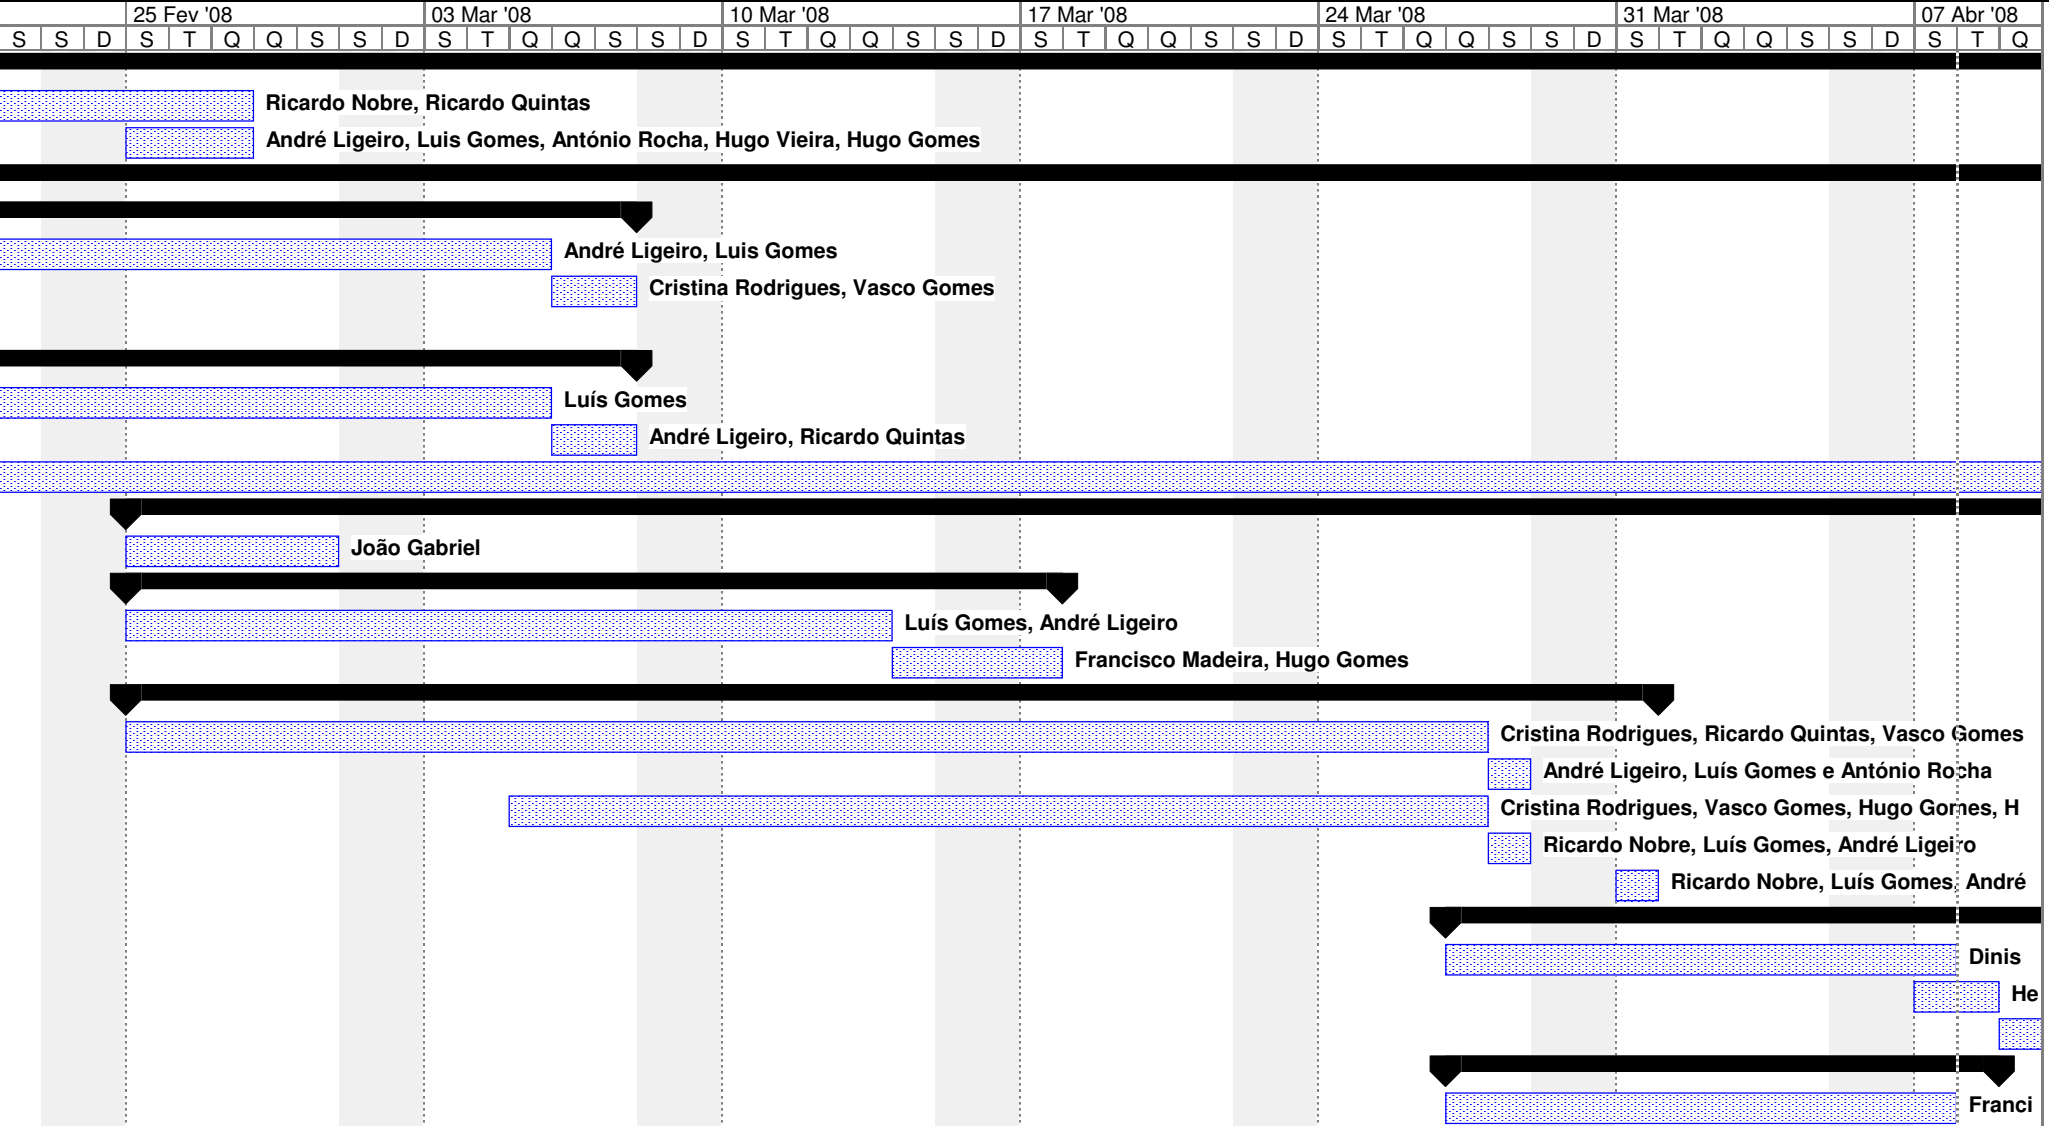

Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08

Tarefa

Progresso

Marco

Sumário

Tarefa Agregada

Marco Agregado

Progresso Agregado


Dividir

Tarefas Externas

Resumo de Projecto

Agrupar por Sumário

Prazo

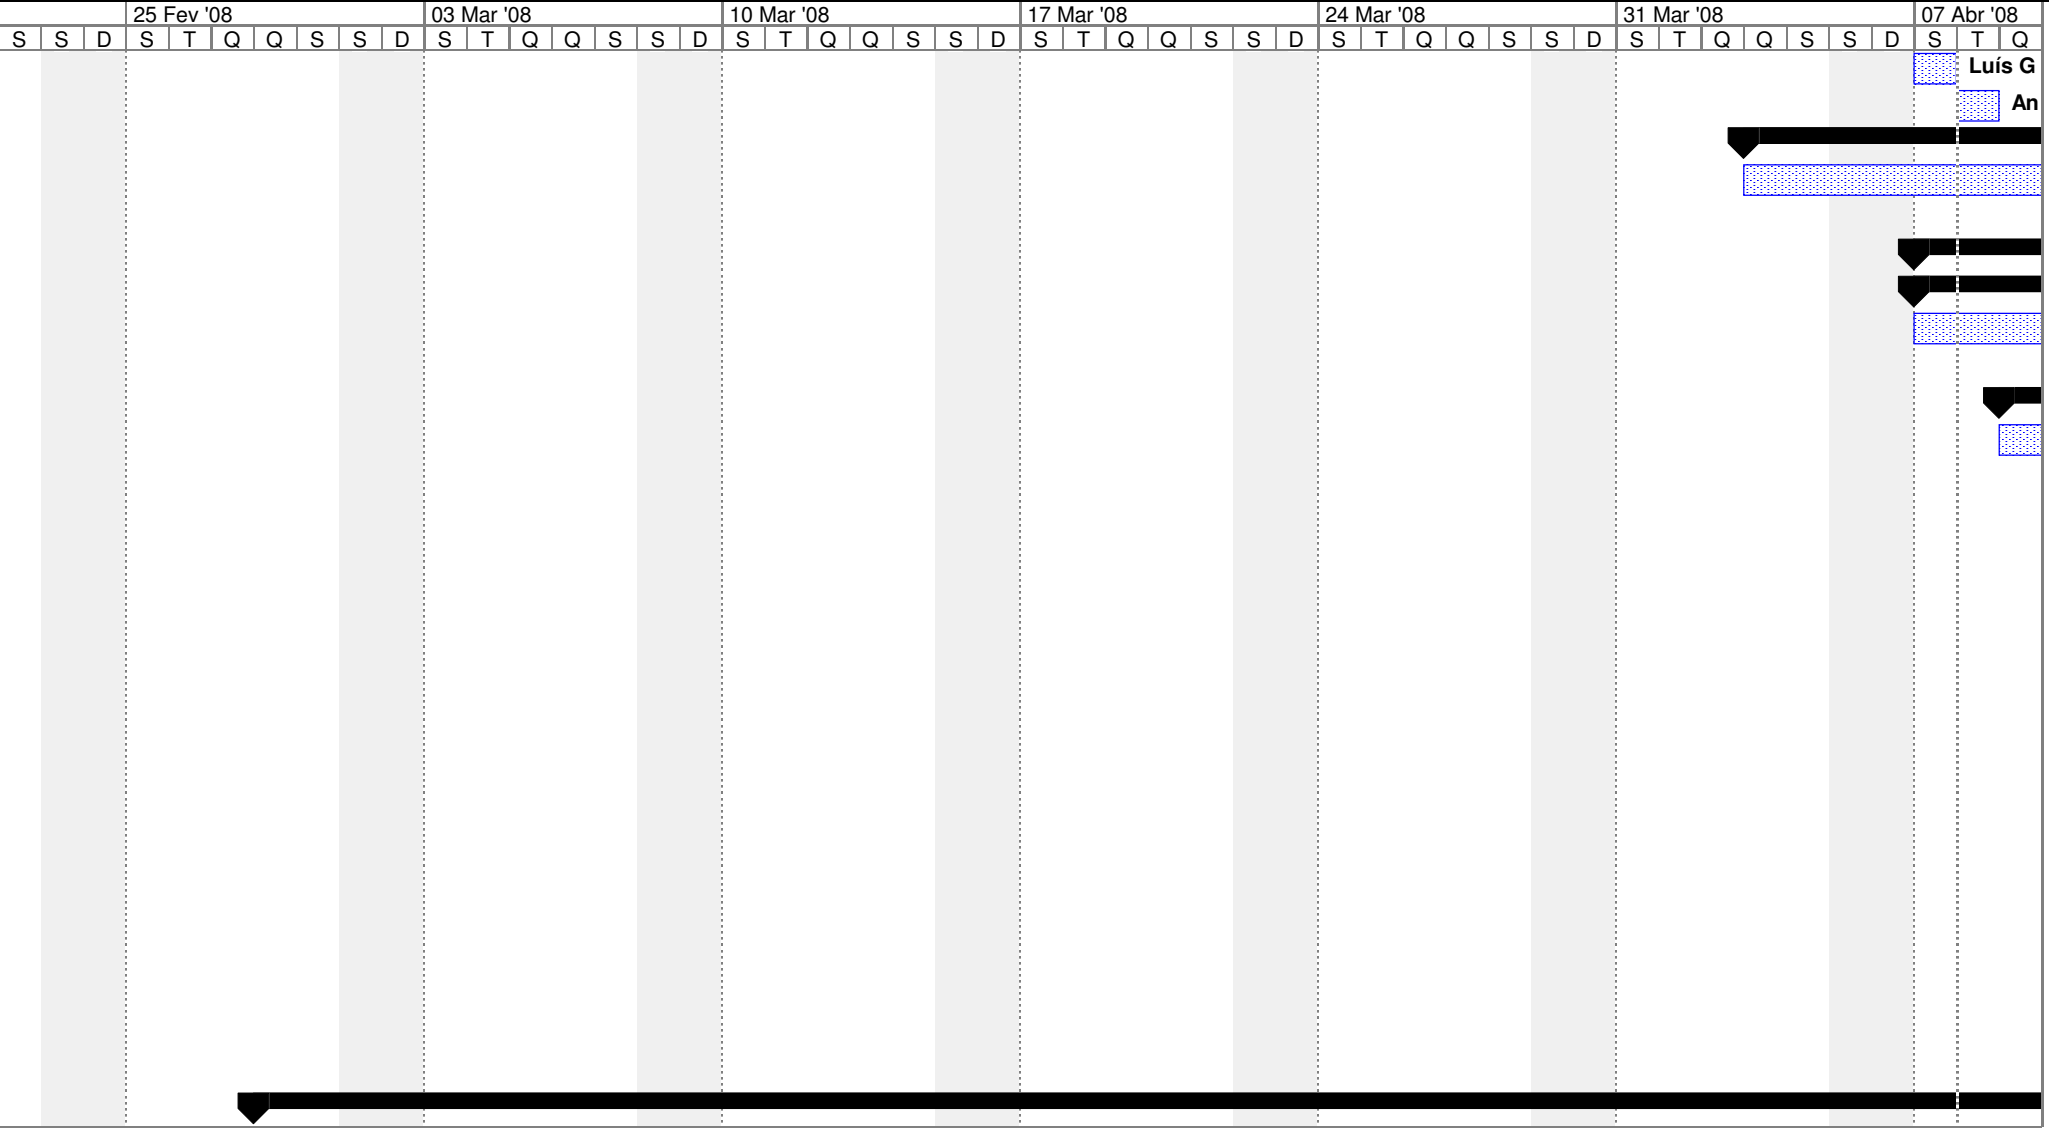

Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08

Tarefa

Progresso

Marco

Sumário

Tarefa Agregada

Marco Agregado

Progresso Agregado

Dividir

Tarefas Externas

Resumo de Projecto

Agrupar por Sumário

Prazo



14 Abr '08 21 Abr '08 28 Abr '08 05 Mai '08 12 Mai '08 19 Mai '08 26 Mai '08

Q S S D S T Q Q S S D S T Q Q S S D S T Q Q S S D S T Q Q S S D S T Q Q S S D S T

**Legend:**


- Tarefa: Blue hatched bar
- Progresso: Solid black bar
- Marco: Black diamond
- Sumário: Black bar with white triangle
- Tarefa Agregada: Blue hatched bar
- Marco Agregado: White diamond
- Progresso Agregado: Solid black bar
- Dividir: Dotted blue line
- Tarefas Externas: Grey bar
- Resumo de Projecto: Grey bar with white triangle
- Agrupar por Sumário: Black bar with white triangle
- Prazo: Green arrow pointing down

**Project Information:**

- Projecto: MAPA DE GANT\_v0.2r
- Data: 08-04-08

**Task Details:**

- Task 1: [Blue hatched bar] (April 14 - April 15)
- Task 2: [Blue hatched bar] (April 15 - April 16)
- Task 3: [Blue hatched bar] (April 16 - April 17)
- Task 4: [Blue hatched bar] (April 17 - April 18)
- Task 5: [Blue hatched bar] (April 18 - April 19)
- Task 6: [Blue hatched bar] (April 19 - April 20)
- Task 7: [Blue hatched bar] (April 20 - April 21)
- Task 8: [Blue hatched bar] (April 21 - April 22)
- Task 9: [Blue hatched bar] (April 22 - April 23)
- Task 10: [Blue hatched bar] (April 23 - April 24)
- Task 11: [Blue hatched bar] (April 24 - April 25)
- Task 12: [Blue hatched bar] (April 25 - April 26)
- Task 13: [Blue hatched bar] (April 26 - April 27)
- Task 14: [Blue hatched bar] (April 27 - April 28)
- Task 15: [Blue hatched bar] (April 28 - April 29)
- Task 16: [Blue hatched bar] (April 29 - April 30)
- Task 17: [Blue hatched bar] (April 30 - May 1)
- Task 18: [Blue hatched bar] (May 1 - May 2)
- Task 19: [Blue hatched bar] (May 2 - May 3)
- Task 20: [Blue hatched bar] (May 3 - May 4)
- Task 21: [Blue hatched bar] (May 4 - May 5)
- Task 22: [Blue hatched bar] (May 5 - May 6)
- Task 23: [Blue hatched bar] (May 6 - May 7)
- Task 24: [Blue hatched bar] (May 7 - May 8)
- Task 25: [Blue hatched bar] (May 8 - May 9)
- Task 26: [Blue hatched bar] (May 9 - May 10)
- Task 27: [Blue hatched bar] (May 10 - May 11)
- Task 28: [Blue hatched bar] (May 11 - May 12)
- Task 29: [Blue hatched bar] (May 12 - May 13)
- Task 30: [Blue hatched bar] (May 13 - May 14)
- Task 31: [Blue hatched bar] (May 14 - May 15)
- Task 32: [Blue hatched bar] (May 15 - May 16)
- Task 33: [Blue hatched bar] (May 16 - May 17)
- Task 34: [Blue hatched bar] (May 17 - May 18)
- Task 35: [Blue hatched bar] (May 18 - May 19)
- Task 36: [Blue hatched bar] (May 19 - May 20)
- Task 37: [Blue hatched bar] (May 20 - May 21)
- Task 38: [Blue hatched bar] (May 21 - May 22)
- Task 39: [Blue hatched bar] (May 22 - May 23)
- Task 40: [Blue hatched bar] (May 23 - May 24)
- Task 41: [Blue hatched bar] (May 24 - May 25)
- Task 42: [Blue hatched bar] (May 25 - May 26)

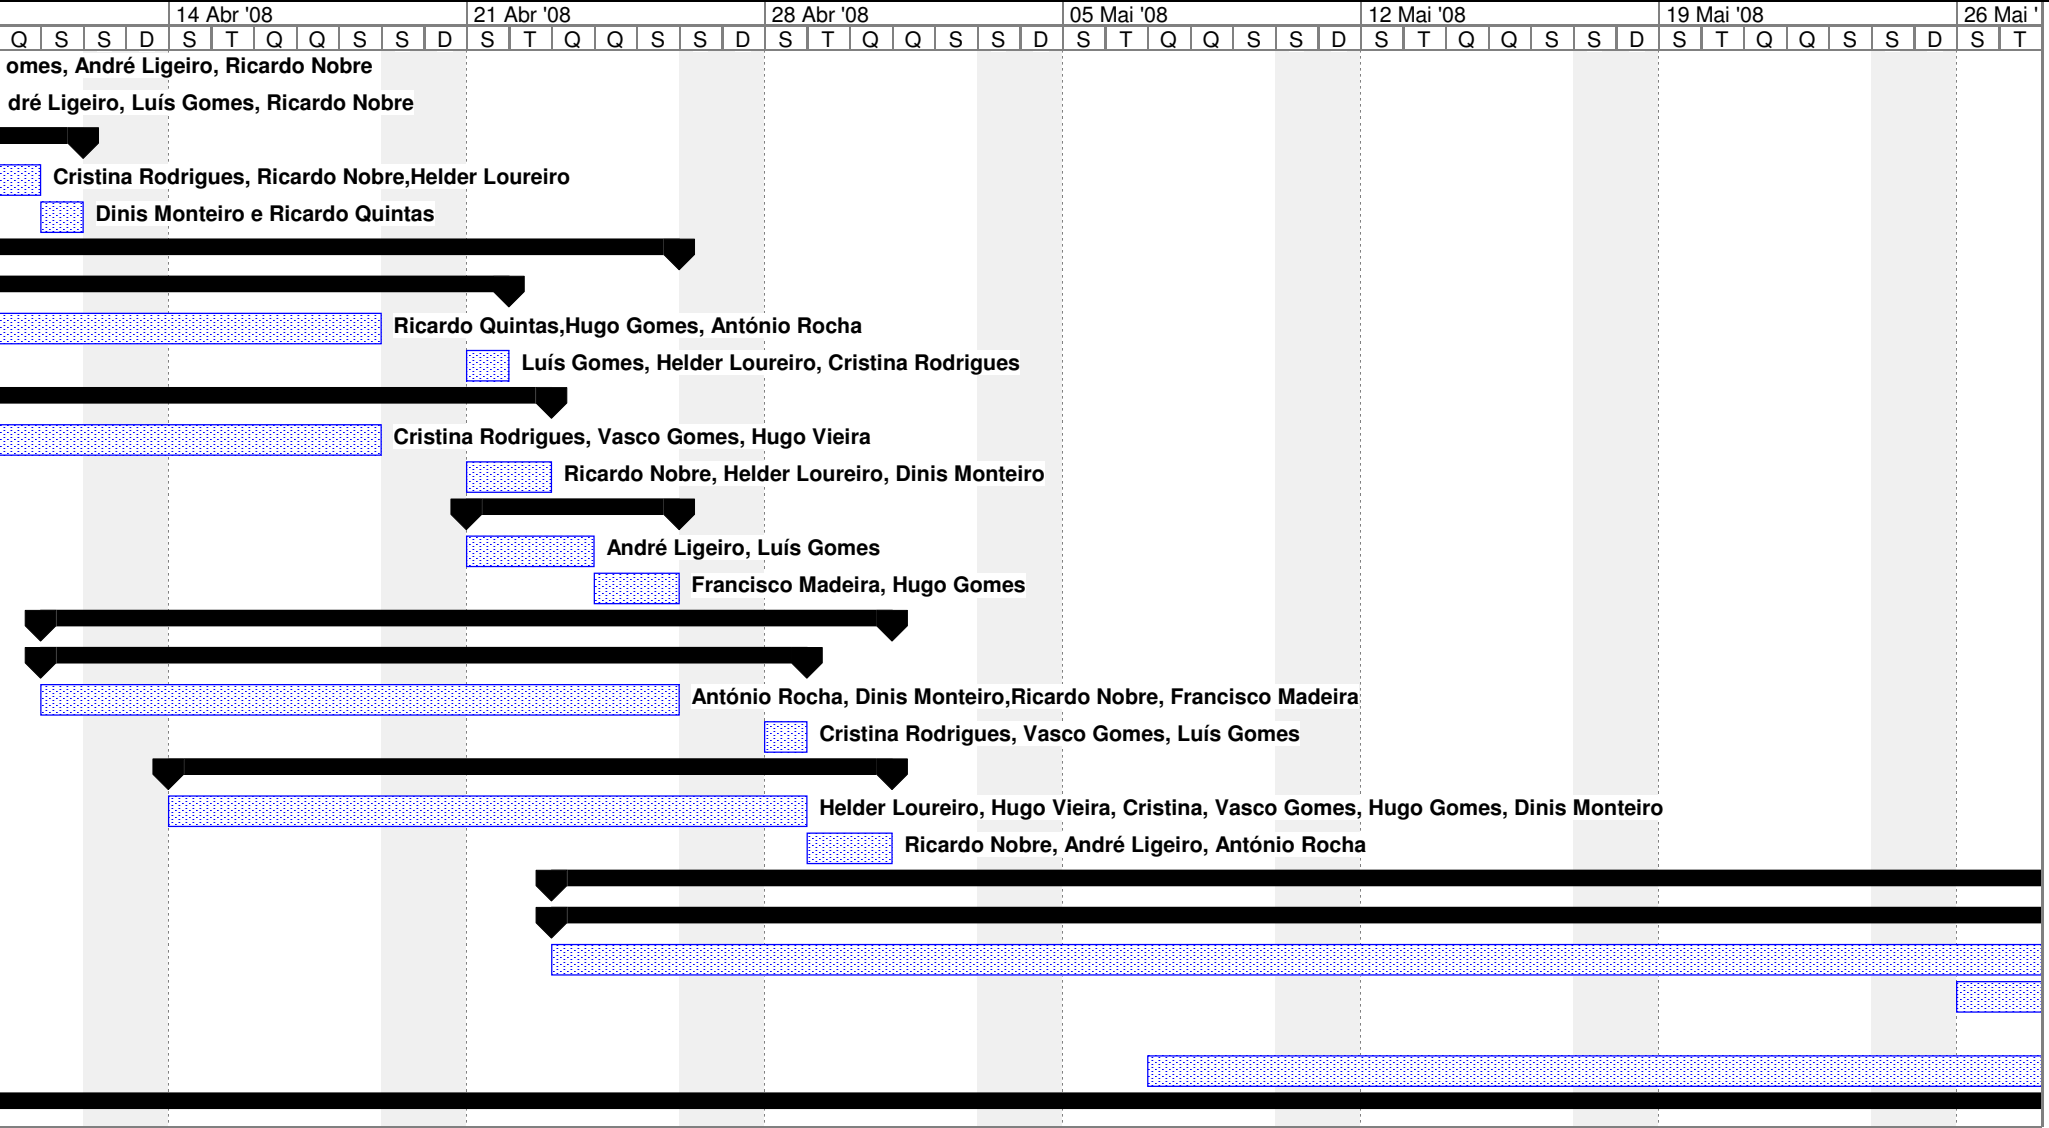

Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08

Tarefa

Progresso

Marco

Sumário

Tarefa Agregada

Marco Agregado

Progresso Agregado

Dividir

Tarefas Externas


Resumo de Projecto

Agrupar por Sumário

Prazo





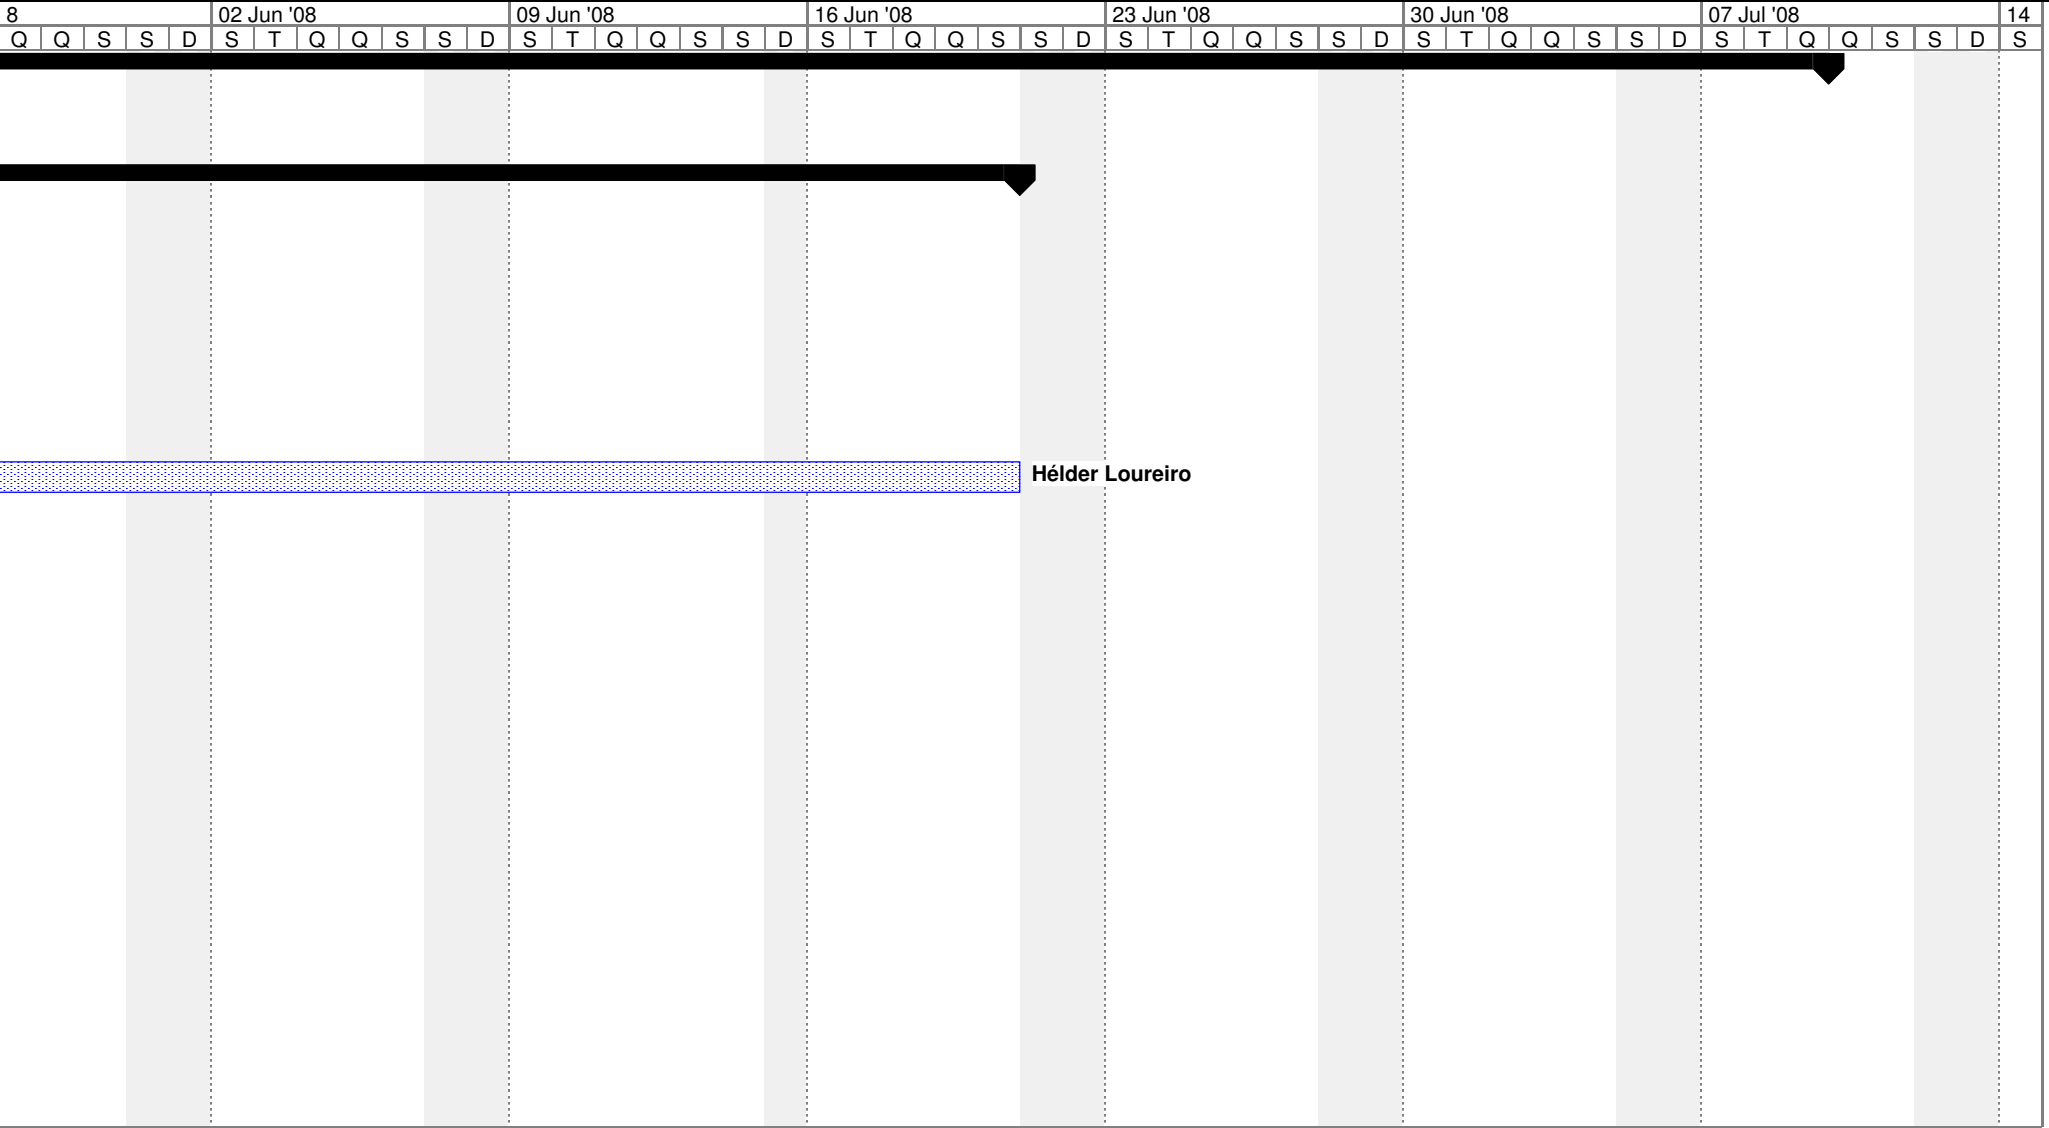

Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08

Tarefa

Progresso

Marco

Sumário

Tarefa Agregada

Marco Agregado

Progresso Agregado


Dividir

Tarefas Externas

Resumo de Projecto

Agrupar por Sumário

Prazo

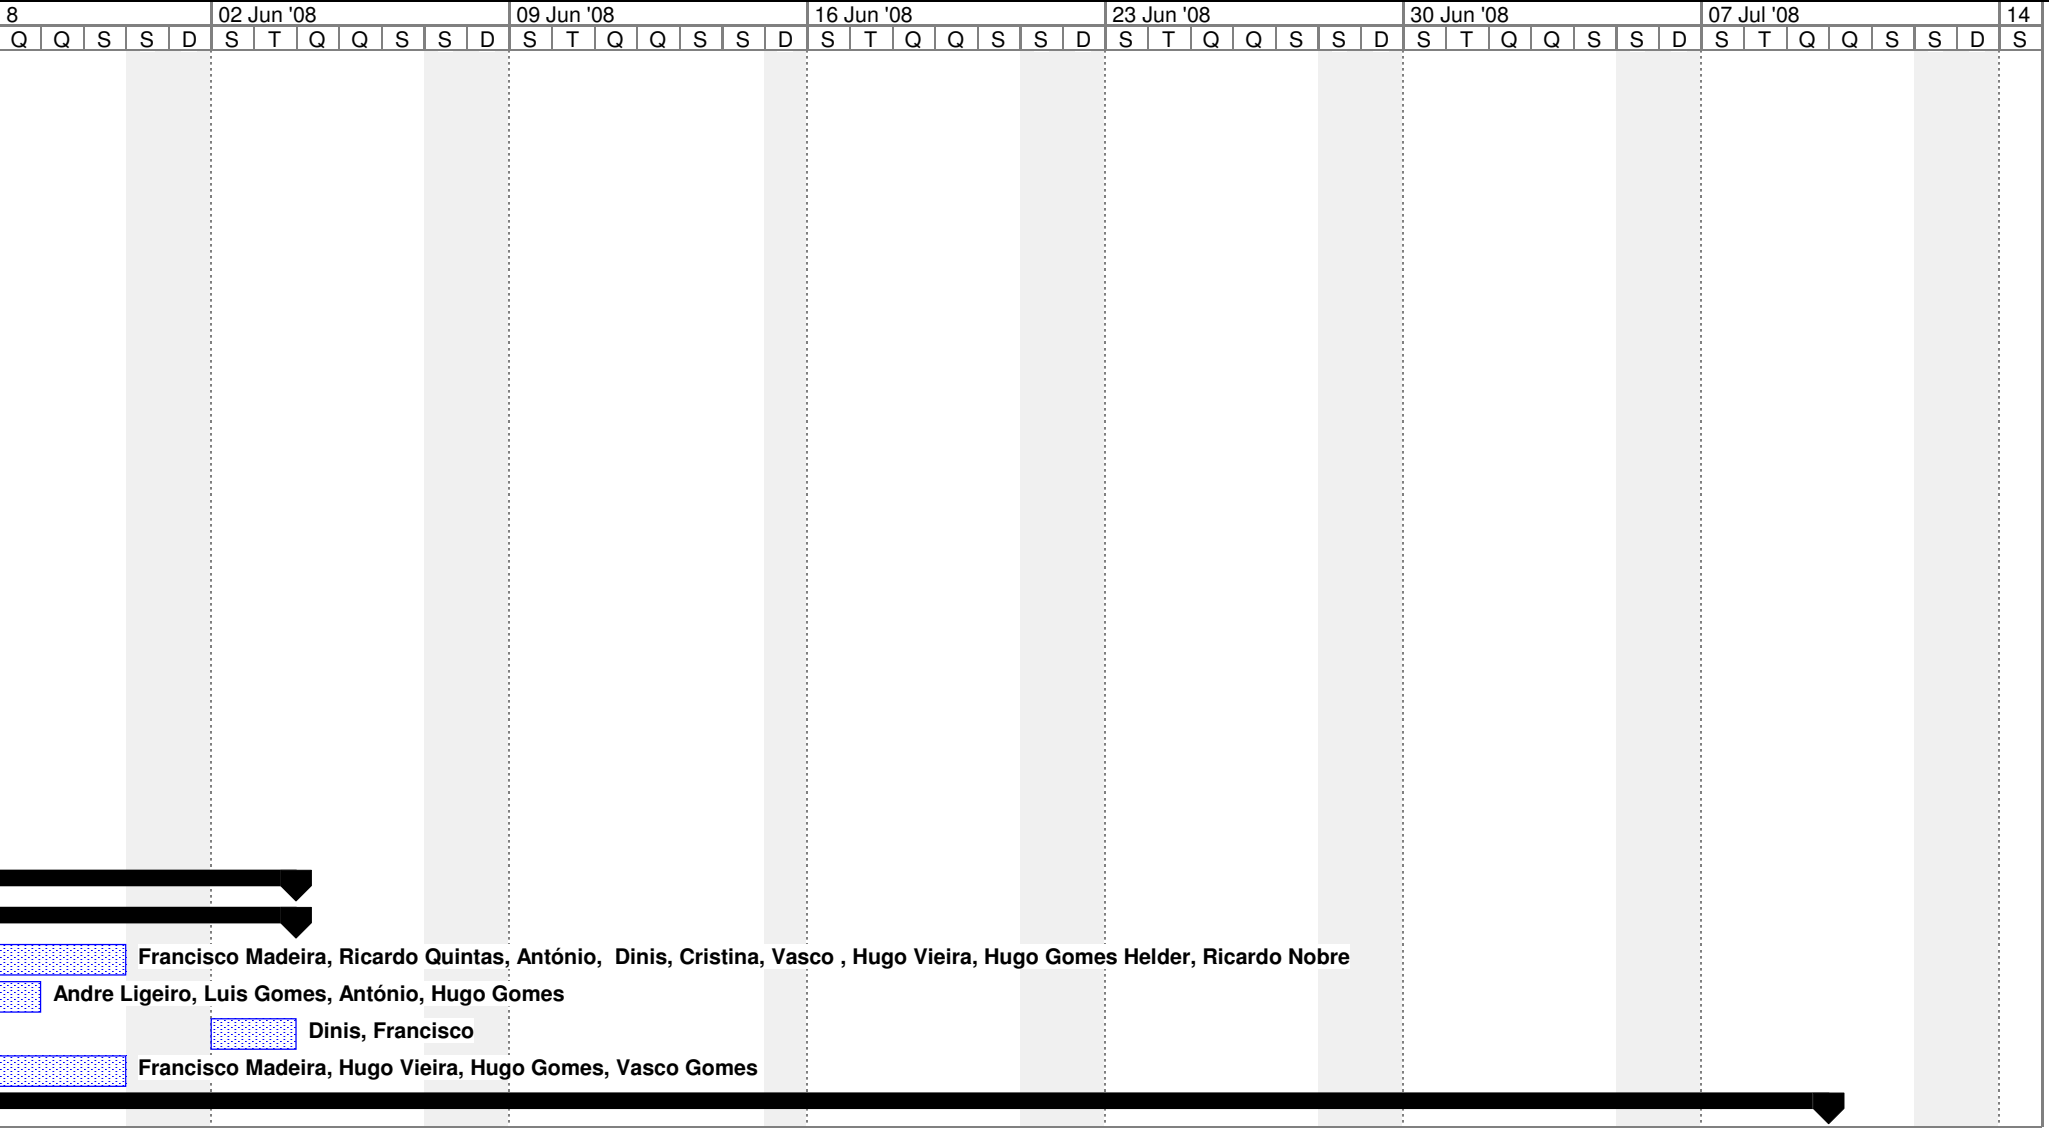


Projecto: MAPA DE GANT\_v0.2r  
Data: 08-04-08


Tarefa


Progresso


Marco

Sumário











Tarefa Agregada


Marco Agregado


Progresso Agregado

Dividir











Tarefas Externas


Resumo de Projecto


Agrupar por Sumário


Prazo









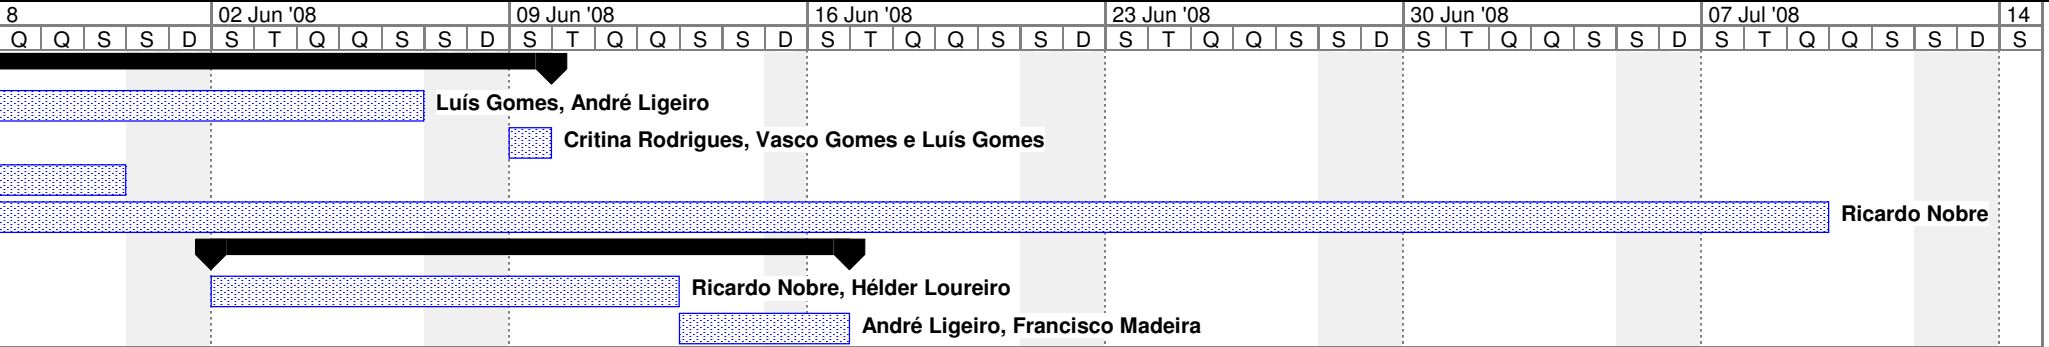

Projecto: MAPA DE GANT_v0.2r Data: 08-04-08	Tarefa		Tarefa Agregada		Tarefas Externas	
	Progresso		Marco Agregado		Resumo de Projecto	
	Marco		Progresso Agregado		Agrupar por Sumário	
	Sumário		Dividir		Prazo	
